

# Program Reporting

Integral planning forecast

Reporting week: 30



## Contents

1. Introduction
2. Forecast delivery planning 6 weeks
3. Delivery planning changes
4. Program consolidated status
5. Project delivery status
6. Overdue deliveries



# 1. Introduction



## Background information

- This slide deck provides a visual presentation of the integral planning the program and is based on detailed planning as published in EPM.
- The slide deck is generated in an automated manner on a weekly basis and reflects the status of the integral planning.

This slide deck consists of the following chapters:

- 1. Introduction
- 2. Forecast delivery planning 6 weeks
- 3. Changes in planned deliveries since the last report
- 4. Consolidated program delivery status per reporting date
- 5. Current project delivery status per reporting date
- 6. Overdue deliveries per project



## 2. Forecast delivery planning 6 weeks



### Planned delivery forecast

	Acceptatie		Acceptatie	Acceptatie	Acceptatie	Acceptatie	
	Week 30 25-jul to 30-jul	Week 31 01-aug to 06-aug	Week 32 08-aug to 13-aug	Week 33 15-aug to 20-aug	Week 34 22-aug to 27-aug	Week 35 29-aug to 03-sep	Week 36 05-sep to 10-sep
98999	• Milestone G5 • Phase G5						
101010						• 101010	• Phase G9



## Planned delivery forecast

	Acceptatie		Acceptatie	Acceptatie	Acceptatie	Acceptatie	
	Week 30 25-jul to 30-jul	Week 31 01-aug to 06-aug	Week 32 08-aug to 13-aug	Week 33 15-aug to 20-aug	Week 34 22-aug to 27-aug	Week 35 29-aug to 03-sep	Week 36 05-sep to 10-sep
PB Airbus 02		• Milestone G5	• Phase G5				
PFS Test with workflow				• PFS Test with workflow	• task 3		



### 3. Delivery planning changes



## Planning changes

Milestones changed since the last report

99999	Milestone G0
99999	Phase G0
99999	Milestone G2
99999	Phase G2
99999	Milestone G5
99999	Phase G5
Airbus T Sample	Identify "To Be" Solution
Airbus T Sample	Design "To Be" Solution
Airbus T Sample	G4 Complete
Airbus T Sample	2. Analysis & Design



| Group Presentation

9



## Planning changes

Milestones changed since the last report

Airbus T Sample	Define Development & Implementation Plan
Airbus T Sample	G5 Commitment to Implement
Airbus T Sample	Phase 2 Cost
Airbus T Sample	Develop Solution
Airbus T Sample	G6 Complete
Airbus T Sample	Test Solution
Airbus T Sample	Accept Solution
Airbus T Sample	G7 Complete
Iololo	Milestone G0
Iololo	Phase G0



| Group Presentation


10



# Planning changes

Milestones changed since the last report

IoIolo Milestone G2
IoIolo Phase G2
IoIolo Milestone G5
IoIolo Phase G5
IoIolo IoIolo
IoIolo Phase G9
IoIolo Milestone G9
jkjkk Task 1
jkjkk jkjkk
jkjkk task 2

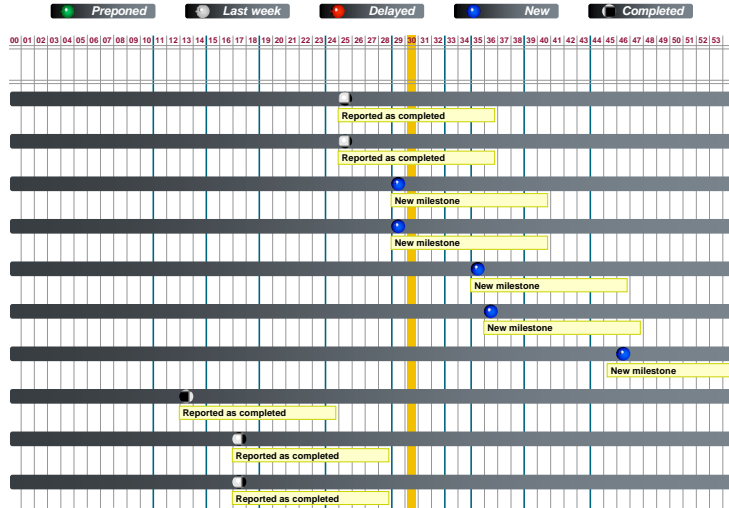

# Planning changes

Milestones changed since the last report

IpIplp Milestone G0
IpIplp Phase G0
IpIplp Milestone G2
IpIplp Phase G2
IpIplp Milestone G5
IpIplp Phase G5
IpIplp Milestone G9
IpIplp Phase G9
no assignmned Milestone G0
no assignmned Phase G0






# Planning changes



# Planning changes

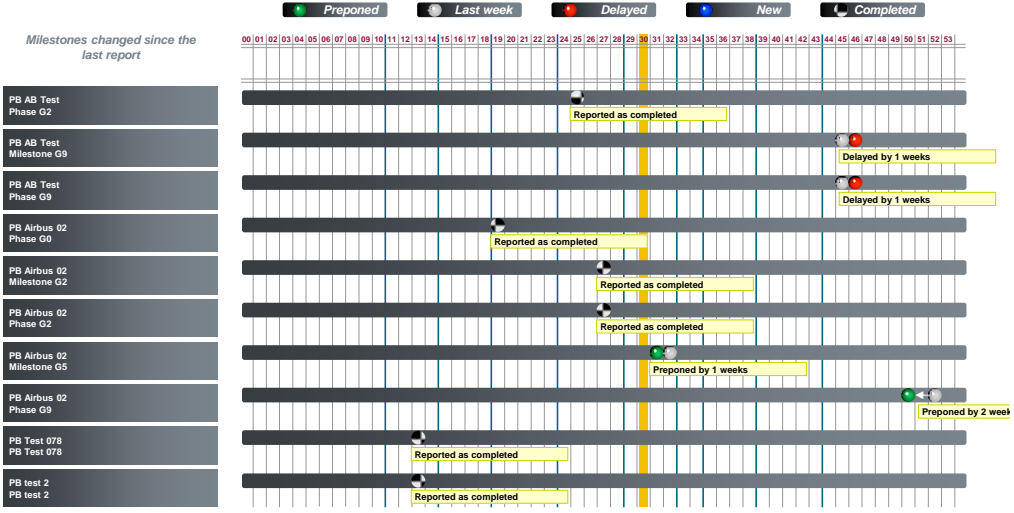




# Planning changes

Milestones changed since the last report


- PB Test Project task 1
- PB Test Project Task 2
- PB Test Project PB Test Project
- PB Test Project Task 3
- PFS Test with workflow task 1
- PFS Test with workflow task 2
- PFS Test with workflow PFS Test with workflow
- PFS Test with workflow task 3
- with ntest template Task 1
- with ntest template task 2

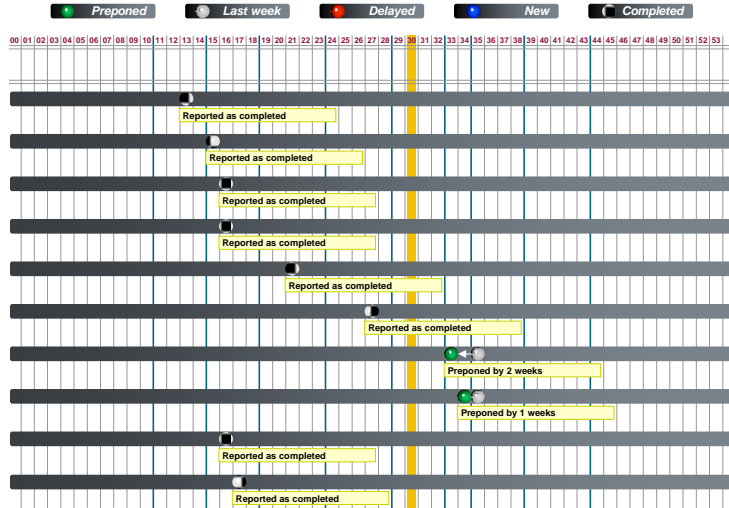

# Planning changes

Milestones changed since the last report

- with ntest template with ntest template

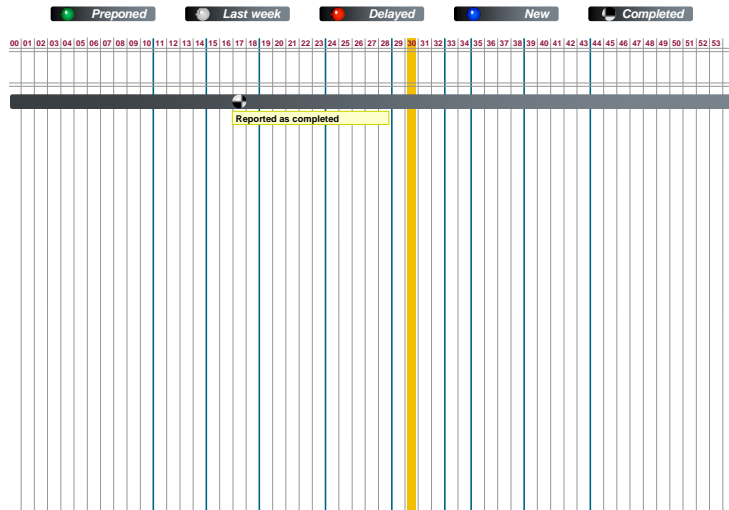






## 4. Program consolidated status




### Program consolidated status

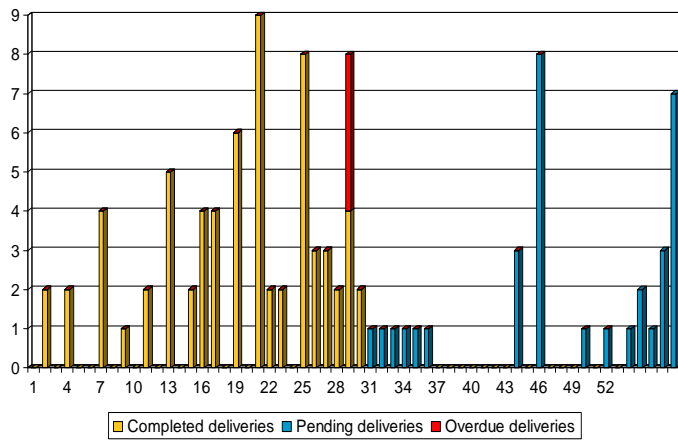



## Program consolidated status





## 5. Project delivery status





## Project delivery status

99999 Airbus T Sample



loloio jkjkjk





| Group Presentation





## Project delivery status

lplplp no assignmentsd



PB AB Test PB Airbus 02




| Group Presentation




## Project delivery status

PB Test 078 PB test 2





PB Test Project PFS Test with workflow



## Project delivery status

Timesheet Administrative Work Items with ntest template





## 6. Overdue deliveries



### Overdue deliveries

Project name	Milestone description	Status	Due date
lololo	Milestone G5	70	18-7-2011 17:00
lololo	Phase G5	70	18-7-2011 17:00
PB AB Test	Milestone G5	0	18-7-2011 17:00
PB AB Test	Phase G5	0	18-7-2011 17:00
Timesheet Administrative Work Item	Timesheet Administrative Work Items	0	
