



**Project for the web**  
**How it works, what you can do**  
**with it!**

**(session 1 of 3)**




January the 11<sup>th</sup>, 2023 @ 12:00 PM EST

Erik van Hurck

# Who is Erik?



**ERIK VAN HURCK**  
Senior consultant @ Projectum

-  <https://www.linkedin.com/in/erikvanhurck>
-  <https://www.theprojectcornerblog.com>
-  <https://www.youtube.com/@theprojectcorner>



30+ client  
implementations and  
training courses



Microsoft Certified



Microsoft Most Valuable Professional  
SINCE 2018

# Agenda

This is part 1 of a 3 part series regarding Project for the web.

Today we discuss **the what** (is P4W).

Next session will be regarding (for) **who** (is P4W).

The week after we will dive deep into **extensibility** options for Project for the web.

# Agenda

- The current state of Project for the web.
- How to create a project.
- How to change default settings and add custom values.
- The latest features that were added by Microsoft.


# Current state of Project for the web

## Continuous improvements

- People tab
- Sprints in Board
- Assignment updates with E3 & E5 license

Stay informed:

[https://bit.ly/MS\\_P4W\\_blog](https://bit.ly/MS_P4W_blog)

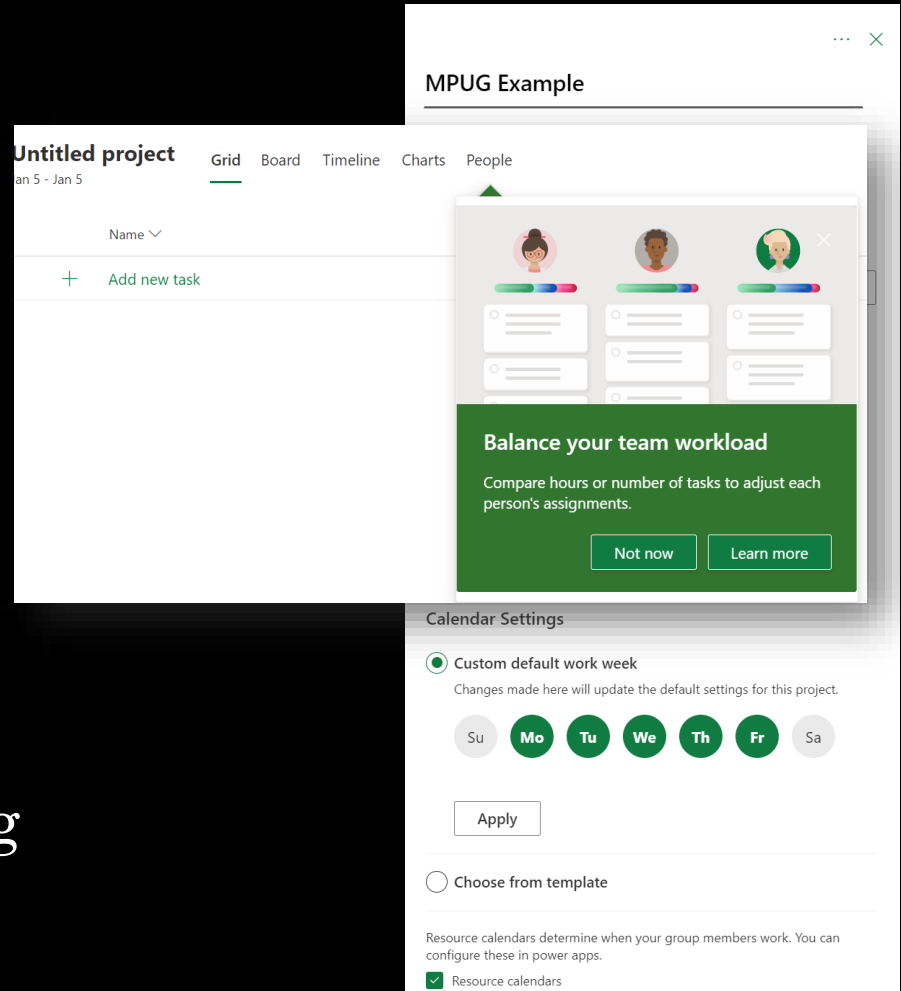

# How to create a project?

A rose by any other name?



Not really, there are differences:

- Project Home
- Project Accelerator
- Custom Model Driven Power Apps
- Project Operations

# Creating a project and making changes

**Commercial Construction** Jan 5, 2023 - May 1, 2024 Grid Board Timeline Charts People

- General Conditions**
  - + Add task
  - Receive notice to proceed and sign contract (3 days) - 01/10
  - Submit bond and insurance documents (2 days) - 01/12
  - Prepare and submit project schedule (2 days) - 01/16
  - Prepare and submit schedule of values (2 days) - 01/18
  - Obtain building permits (4 days) - 01/16
  - Submit preliminary shop drawings (2 weeks) - 01/30
  - Submit monthly requests for payment (1 day) - 01/11
- Long Lead Procurement**
  - + Add task
  - Submit shop drawings and order long lead items - steel (2 weeks) - 01/25
  - Submit shop drawings and order long lead items - roofing (2 weeks) - 02/13
  - Submit shop drawings and order long lead items - elevator (2 weeks) - 02/13
  - Submit shop drawings and order long lead items - plumbing (2 weeks) - 02/13
  - Submit shop drawings and order long lead items - electric (2 weeks) - 02/13
  - Submit shop drawings and order long lead items - HVAC (2 weeks) - 02/13
  - Detail, fabricate and deliver steel (12 weeks) - 04/19
- Mobilize on Site**
  - + Add task
  - Install temporary power (2 days) - 01/12
  - Install temporary water service (2 days) - 01/12
  - Set up site office (3 days) - 01/17
  - Set line and grade benchmarks (3 days) - 01/20
  - Prepare site - lay down yard and temporary fencing (2 days) - 01/24
- Site Grading and Utilities**
  - + Add task
  - Clear and grub site (3 days) - 01/27
  - Stone site access and temporary parking area (2 days) - 01/31
  - Rough grade site (cut and fill) (1 week) - 02/07
  - Install storm drainage (2 weeks) - 02/21
  - Install exterior fire line and building fire riser (2 weeks) - 02/21
  - Perform final site grading (2 weeks) - 03/07
  - Erect building batter boards and layout building (1 week) - 03/14
- Foundations**
  - + Add task
  - Excavate foundations (2 weeks) - 03/28
  - Excavate elevator pit (2 days) - 03/16
  - Form column piers and spread foundations (4 days) - 04/03
  - Rough-in electric and plumbing in elevator (4 days) - 03/22
  - Form elevator pit walls (4 days) - 03/28
  - Set reinforcing and anchor bolts (4 days) - 04/07
  - Pour column piers and foundations (5 days) - 04/14
  - Pour concrete elevator walls (1 day)
- Form and Pour Concrete - Floo...**
  - + Add task
  - Form 2nd floor including all floor openings (5 days) - 07/07
  - Install rebar and in-floor utilities (including mechanical, electrical, plumbing) (5 days) - 05/19
  - Pour 2nd floor slab (4 days) - 07/13
  - Cure 2nd floor slab (7 days) - 07/24
  - Strip forms from 2nd floor slab (2 days) - 07/26
  - Form 3rd floor including all floor openings (5 days) - 07/31
  - Install rebar and in-floor utilities (including mechanical, electrical, plumbing) (5 days) - 07/31
- Carpentry Work**
  - + Add task
  - Install exterior sheathing and metal studs (3 weeks) - 09/29





# Latest additions to Project for the web

- People tab
- Sprints
- Calendar alterations
- What would you like to see in the tool next?

Let's discuss this next week during the second session.





**Thank You!**

**How it works, what you  
can do with it!**

**(session 1 of 3)**

**Erik van Hurck**

[Erik@theprojectcornerblog.com](mailto:Erik@theprojectcornerblog.com)

@ErikvanHurck
